


**DIRECCIÓN GENERAL DE INFRAESTRUCTURA SOCIAL
GRAFICA DE AVANCE FISICO Y FINANCIERO
PROGRAMADO Vs REAL**

CONTRATO						
FECHA	SEM 1 20-25 NOV	SEM 2 26 NOV-02 DIC	SEM 3 03-09 DIC	SEM 4 10-16 DIC	SEM 5 17-23 DIC	SEM 6 24-31 DIC
SEMANAL	\$151.012.93 20.02%	\$151.088.36 20.03%	\$113.071.12 14.99%	\$113.071.12 14.99%	\$113.071.12 14.99%	\$112.995.69 14.98%
ACUMULADO	\$151.012.93 20.02%	\$302.101.29 40.05%	\$415.172.41 55.04%	\$528.243.53 70.03%	\$641.314.65 85.02%	\$754.310.34 100.00%

EJECUTADO REAL						
FECHA	SEM 1 20-25 NOV	SEM 2 26 NOV-02 DIC	SEM 3 03-09 DIC	SEM 4 10-16 DIC	SEM 5 17-23 DIC	SEM 6 24-31 DIC
SEMANAL	\$71.206.90 9.44%	\$256.616.38 34.02%	\$181.034.48 24.00%	\$132.079.74 17.51%	\$75.431.03 10.00%	\$37.941.81 5.03%
ACUMULADO	\$71.206.90 9.44%	\$327.823.27 43.46%	\$508.857.76 67.46%	\$640.937.50 84.97%	\$716.368.53 94.97%	\$754.310.34 100.00%

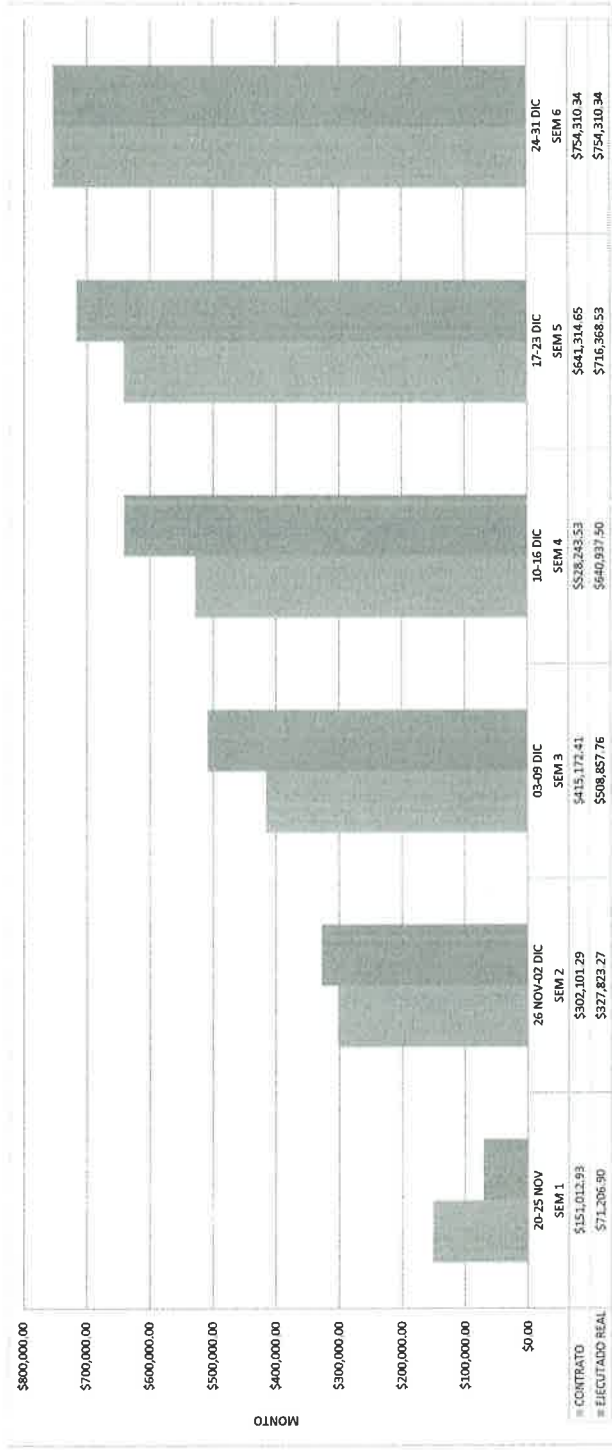

No. Y NOMBRE DE LA OBRA: C-00077/0092 AMPLIACION DE RED DE ALCANTARILLADO EN COLONIA JAVIER LAMARQUE CANO DE PUEBLO YAQUI, CAJEME.

CONTRATO: SEDESSON-FISE-2017-090.

SUPERVISIÓN DEPENDENCIA
SEDESSON

[Signature]

ARQ. HUGO MENDOZA LEON
