


DIRECCIÓN GENERAL DE INFRAESTRUCTURA SOCIAL
GRAFICA DE AVANCE FISICO Y FINANCIERO
PROGRAMADO Vs REAL

CONTRATO			
FECHA	SEM 1 27-30 NOV	SEM 2 01-07 DIC	SEM 3 08-12 DIC
SEMANAL	\$19,894.91 6.50%	\$138,866.50 45.37%	\$147,314.18 48.13%
ACUMULADO	\$19,894.91 6.50%	\$158,761.41 51.87%	\$306,075.59 100.00%

EJECUTADO REAL			
FECHA	SEM 1 27-30 NOV	SEM 2 01-07 DIC	SEM 3 08-12 DIC
SEMANAL	\$45,911.34 15.00%	\$137,734.02 45.00%	\$122,430.24 40.00%
ACUMULADO	\$45,911.34 15.00%	\$183,645.35 60.00%	\$306,075.59 100.00%

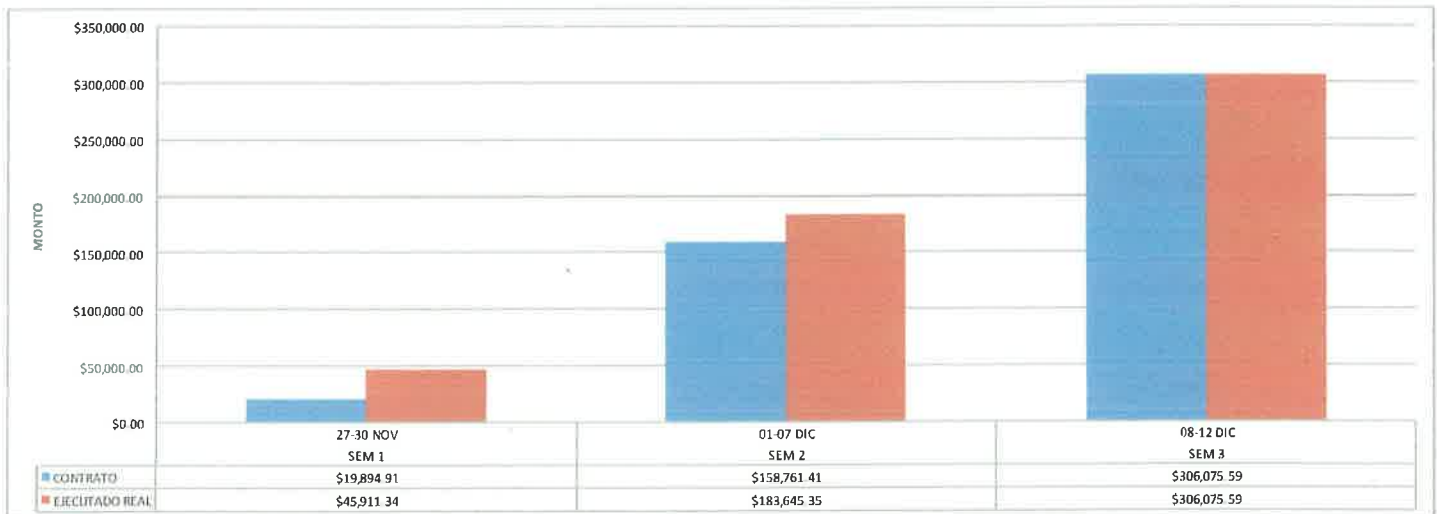

No. Y NOMBRE DE LA OBRA: C-00077/0094 AMPLIACION DE RED DE ALCANTARILLADO EN COLONIA MEZQUITE, MAGDALENA DE KINO.

CONTRATO: SEDESSON-FISE-2017-095.

SUPERVISIÓN DEPENDENCIA
SEDESSON

ING. SERGIO DIAZ PEÑA

SUPERVISIÓN EXTERNA
GRUPO JASMAA, S.A. DE C.V.

C. JUAN ADOLFO SHWARZBECK ARTEE
