




DIRECCIÓN GENERAL DE INFRAESTRUCTURA SOCIAL
GRAFICA DE AVANCE FISICO Y FINANCIERO
PROGRAMADO Vs REAL

CONTRATO				
FECHA	SEM 1 20-30 NOV	SEM 2 01-07 DIC	SEM 3 08-14 DIC	SEM 4 15-18 DIC
SEMANAL	\$43,908.75 13.50%	\$76,504.11 23.52%	\$140,768.21 43.28%	\$64,068.95 19.70%
ACUMULADO	\$43,908.75 13.50%	\$120,412.87 37.02%	\$261,181.07 80.30%	\$325,250.02 100.00%

EJECUTADO REAL				
FECHA	SEM 1 20-30 NOV	SEM 2 01-07 DIC	SEM 3 08-14 DIC	SEM 4 15-18 DIC
SEMANAL	\$46,842.47 14.40%	\$76,417.60 23.50%	\$160,950.29 49.49%	\$41,039.66 12.62%
ACUMULADO	\$46,842.47 14.40%	\$123,260.06 37.90%	\$284,210.36 87.38%	\$325,250.02 100.00%

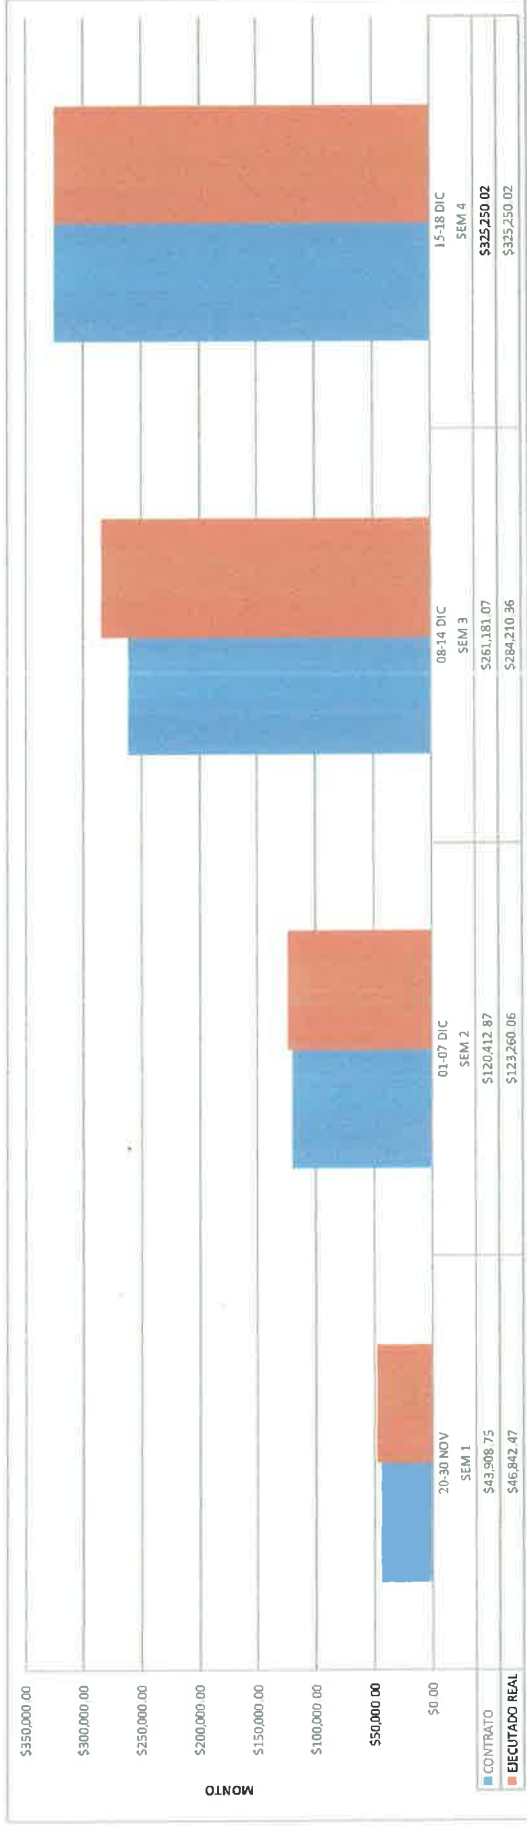

No. Y NOMBRE DE LA OBRA: C-00077/0091 AMPLIACION DE LA RED DE DRENAJE SANITARIO EN AVENIDA LIRIO Y GIRASOL, COLONIA ADOLFO LOPEZ MATEOS, HERMOSILLO SONORA.
CONTRATO: SEDESSON-FISE-2017-087.

SUPERVISIÓN DEPENDENCIA
SEDESSON

ING. SÉRGIO DÍAZ PEÑA

SUPERVISIÓN EXTERNA
GRUPO JASMAA, S.A. DE C.V.

C. JUAN ADOLFO SHWARZBECK ARTEE
