


DIRECCIÓN GENERAL DE INFRAESTRUCTURA SOCIAL
GRAFICA DE AVANCE FISICO Y FINANCIERO
PROGRAMADO Vs REAL

CONTRATO					
FECHA	SEM 1 18-31 OCT	SEM 2 01-07 NOV	SEM 3 08-14 NOV	SEM 4 15-21 NOV	SEM 5 22-30 NOV
SEMANAL	\$133,140.75 12.37%	\$189,217.01 17.58%	\$242,817.74 22.56%	\$378,003.50 35.12%	\$133,140.75 12.37%
ACUMULADO	\$133,140.75 12.37%	\$322,357.77 29.95%	\$565,175.50 52.51%	\$943,179.00 87.63%	\$1,076,319.75 100.00%

EJECUTADO REAL					
FECHA	SEM 1 18-31 OCT	SEM 2 01-07 NOV	SEM 3 08-14 NOV	SEM 4 15-21 NOV	SEM 5 22-30 NOV
SEMANAL	\$170,131.41 15.81%	\$183,652.26 17.06%	\$247,768.92 23.02%	\$402,579.31 37.40%	\$72,187.86 6.71%
ACUMULADO	\$170,131.41 15.81%	\$353,783.67 32.87%	\$601,552.58 55.89%	\$1,004,131.89 93.29%	\$1,076,319.75 100.00%

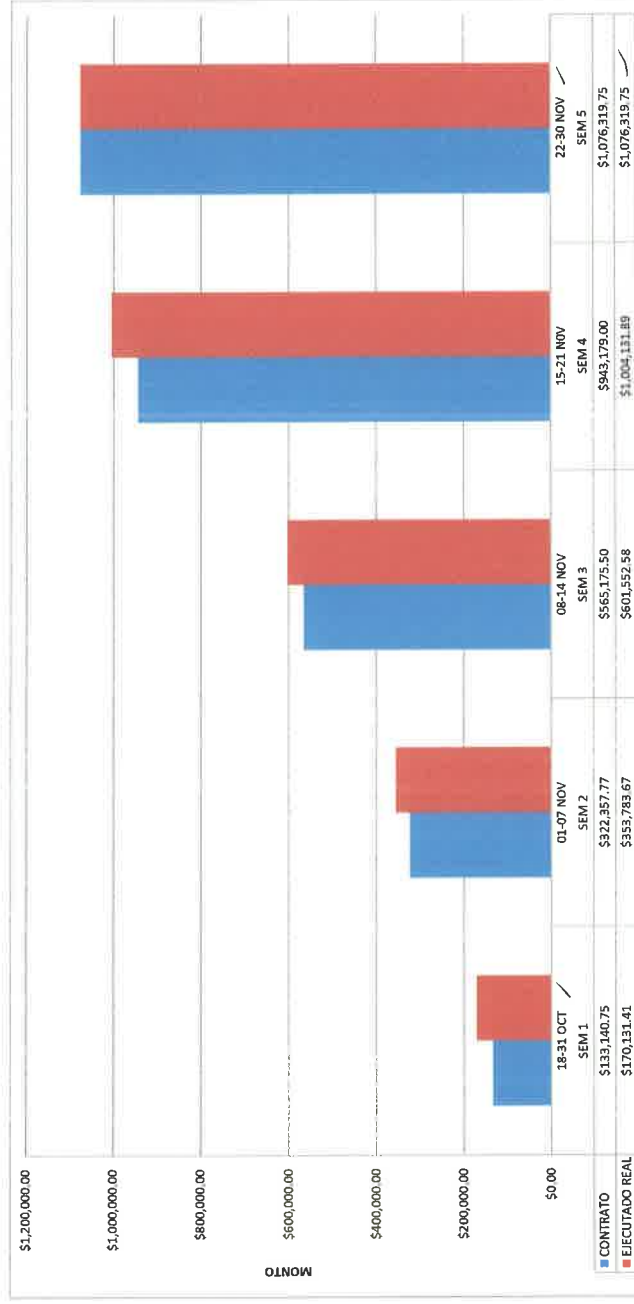

No. Y NOMBRE DE LA OBRA : C-00075/0317 AMPLIACION DE VIVIENDA EN VARIAS LOCALIDADES DEL MUNICIPIO DE VILLA PESQUEIRA.
 CONTRATO: SEDESSON-FISE-2017-084.

SUPERVISIÓN DEPENDENCIA
 SEDESSON
 ING. SERGIO DIAZ PEÑA

SUPERVISIÓN EXTERNA
 RAZA ESTRUCTURAS METALICAS CIVILES,
 ING. ROSARIO QSVATBO ZAVALA ESQUER
