


DIRECCIÓN GENERAL DE INFRAESTRUCTURA SOCIAL
GRAFICA DE AVANCE FISICO Y FINANCIERO
PROGRAMADO Vs REAL

CONCENTRADO SEMANAL		SEM 1	SEM 2	SEM 3	SEM 4
		9-15 OCT	16-31 OCT	1-15 NOV	16-30 NOV
CONTRATO		\$76,104.46	\$81,178.10	\$78,641.28	\$78,641.28
EJECUTADO REAL		\$95,904.00	\$95,904.00	\$63,936.00	\$58,821.12

ACUMULADO SEMANAL		SEM 1	SEM 2	SEM 3	SEM 4
		9-15 OCT	16-31 OCT	1-15 NOV	16-30 NOV
CONTRATO		\$76,104.46	\$157,282.56	\$235,923.84	\$314,565.12
EJECUTADO REAL		\$95,904.00	\$191,808.00	\$255,744.00	\$314,565.12

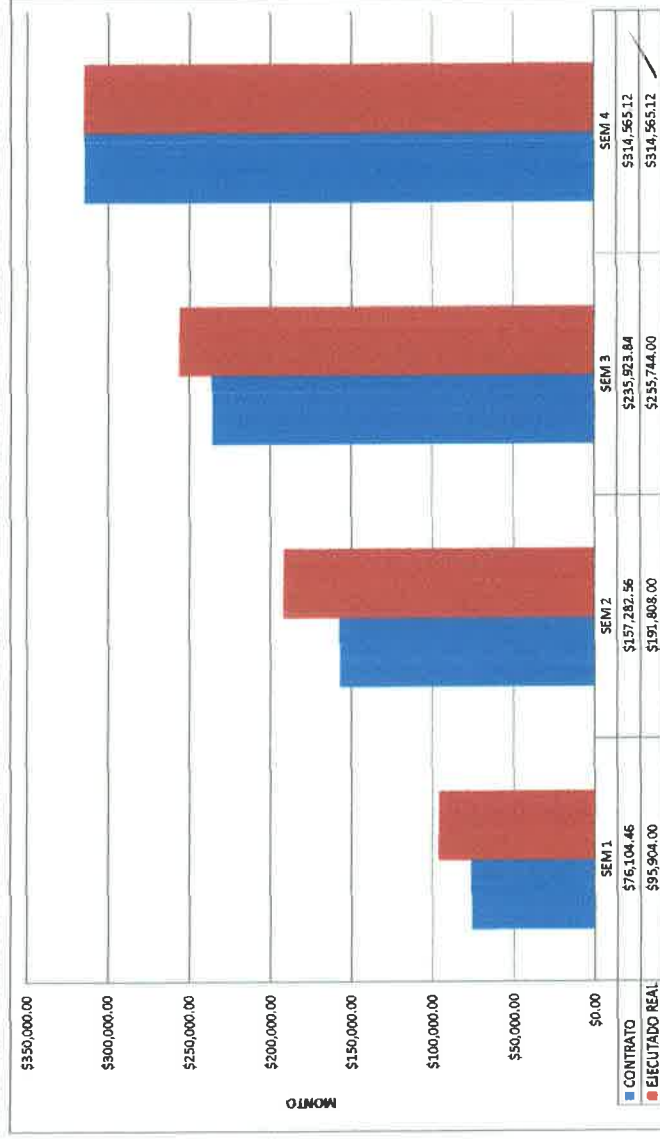

No. Y NOMBRE DE LA OBRA : C-00075/0353 CONSTRUCCION DE PISO FIRME EN FRANCISCO JAVIER MINA (CAMPO 60)

CONTRATO: SEDESSON-FISE-2017-079

SUPERVISIÓN DEPENDENCIA
SEDESSON

SUPERVISIÓN EXTERNA
DAPCI, S. A. DE C. V.

ING. SERGIO DIAZ PEÑA

ING. ROBERTO GAMBOA MORALES
